



# GREENPORT SCHOOLS

## 2021 Bond Referendum Status Report



# Locker Room Scope:

Girl's Locker room:

- New floors provided
- New lockers provided
- New paint on walls/ceiling's/doors and frames

**Girl's locker room Before:**




**Girl's locker room After:**



**Boy's locker room Before:**



**Boy's locker room After:**

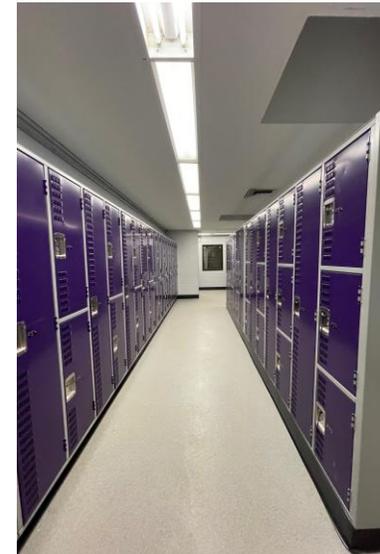

Boy's Locker room:

- New floors provided
- New lockers provided
- New paint on walls/ceiling's/doors and frames
- New storage room provided



Construction Management & Consulting Services

# Cabling/ Camera/ Security Upgrades Scope:


Cabling/ Camera/ Security Upgrades Scope:

- New P.A. system
- New security cameras provided for exterior and interior of building

Remaining Contract Work:

- Wall mounted speakers
- Final programming for P.A. system
- Final camera system programming

Photos :

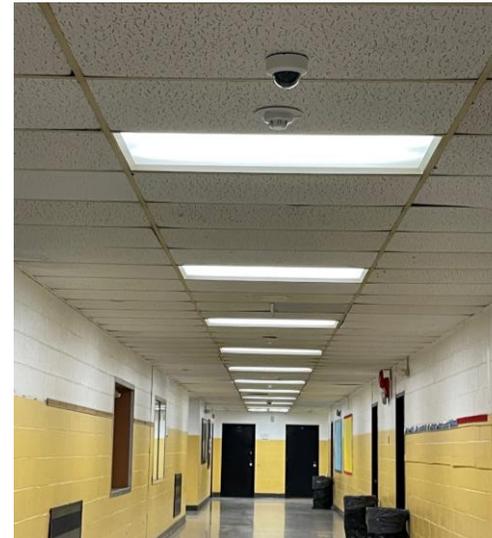

# Masonry Restoration:

Masonry restoration Scope:

- Repoint brick
- Power wash

Remaining Contract Work:

- Replace sealant
- Water proof system
- Repaint specified entrances
- New cap stones

Photos :



Construction Management & Consulting Services

# Proposed timeline:

## **Greenport Project B – Phase I**

Interior Door Replacement & Hardware

Existing Elementary Library Room 112 (Home/Careers 112)

Existing H&C 117 Becomes DO/Business Office 117

Main Power Conversion

Aux Gym

## **Phase II**

Student Toilet Renovations

RTU – Existing Gym & Locker Rooms

Dust Collector

Shop Class – Existing

Existing Rooms 309/308 Reno TV Studio/Control Rm.

Elementary Library Relocated to 105

Unit Ventilators in Classrooms 1<sup>st</sup> Floor

Existing DO/BO Becomes HS Office/Guidance Office Rms 109 and 110

Existing Class Room 106 Becomes HS Office 106

Existing Class Room 111 Becomes SW/Psych Office Suite

Existing Office Room 133 Becomes Chorus 133

Existing HS Office (Room 305) Becomes Classroom 305

# Proposed timeline:

## **Phase III**

Floor Tile Replacement – 2<sup>nd</sup>/3<sup>rd</sup> Floors (Possible Alternate)

Corridor Lockers (By District Contract)

Unit Ventilators 2<sup>nd</sup>/3<sup>rd</sup> Floors

Electrical Panels

## **Alternates as discussed:**

- TV Studio Room 309
- Multipurpose Room 135
- Wall Panels at Multipurpose Room 135
- Trophy/Display Cases
- General Science Room 315
- Elementary Library Room 105 'Cloud' Ceiling System
- Art Room 115
- Secondary Library Room 307
- O/H Door Replacement (CR23/2 and CR24/2)
- ROTC Room #B-4
- New Vehicle Lift at Auto Shop
- Second Floor VAT Tile Replacement
- Third Floor VAT Tile Replacement
- Second Floor Door and Hardware Replacement
- Third Floor Door and Hardware Replacement
- Moisture Control System at New Floor Slab
- Chorus Room 133 New Acoustical
- Pre-K Toilet Room CR-19A
- Toilet Room 223A
